



ARCHITECTS CLIENT FOCUSED. PASSION DRIVEN.

FIELD REPORT 44

Project: Muir High School Modernization
0913900.52 /A#03-115534
Muir High School Gymnasium Bleachers
1020701.52/A#03-116700
Muir High School Kitchen Modernization
1114900.52/A#03-115819

Meeting Date: October 3, 2017

Members Present:

George Kwiter, Pasadena Unified School District
Vinny Nazerian, The Nazerian Group
Robert Abolian, The Nazerian Group
Mardik Eskandarian, The Nazerian Group
Gregory L. Hankins, Knowland Construction Services
Daryl Van Dran, WLC Architects, Inc.

Distribution:

Nelson Cayabyab, Pasadena Unified School District
Miguel Perez Escalona, Pasadena Unified School District
Greg Torosyan, The Nazerian Group
Vartan Nazerian, The Nazerian Group
Robert Hensley, WLC Architects, Inc.
Konni Wong, WLC Architects, Inc.

PROGRESS SCHEDULE

Start Date	Contract Time (Days)	Completion Date (Orig.)	Weather Extension (Days)	Other Extension (Days)	Completion Date (Rev.)	Days Left To Complete
09/19/16	545	03/18/18	000	000	00/00/00	161

Projects	Estimated Project Completion Percentage per IOR Verified Report
Modernization / A #03-115534	55%
Kitchen / A #03-115819	55%
Gym Bleachers / A #03-116700	70%

WORK IN PROGRESS

1. Wooden seats, seat backs, and stanchions have been removed and have been staged in the theatre. Per the Contract Documents, the Contractor is to provide a preliminary site survey per 1.4 of the Theater Seating Renovation Specifications, 12611. To date, no site survey has been received. **No substitution request has been received from Contractor as of May 9, 2017. The Contractor provided COP 012 on May 15, 2017 that only listed costs. On May 16, 2017, the Architect requested a complete seating package for review by the District and Architect. A floor plan was received and returned for revision by the Contractor. No seating materials information received as of September 19, 2017. The Contractor promised the full submittal by next week. As of October 3, 2017, no submittal has been received.**

2. Utility rough-ins at the Kitchen, Cafeteria and mechanical room are ongoing. Structural steel has resumed at the low roof structure. Site work at the Mustang Café has resumed.

3. Proposal Request 01 was generated in response to the District-requested storm drain revisions. COP 22 was received from the Contractor September 19, 2017 and was reviewed by the Civil Engineer. Revisions were requested and a revised COP 22 was received. **On September 26, 2017, the District stated that they would pursue two outside quotes for the same work. If there is a cost savings, the work could be performed by others as a subcontractor to the Contractor. As of October 3, 2017, the District has not decided on a course of action.**

4. Fire alarm work at Buildings D and G is nearing completion. On September 19, 2017, the Electrical Engineer visited the site to review field conditions. After the meeting, the District requested a cost proposal from the Contractor to combine the existing F.A. controls into the new F. A. control cabinet in lieu of installing the new cabinet in the adjacent room. As of October 3, 2017, no cost proposal has been received.

**CHANGE ORDER PROPOSAL LOG
 Mod. A#03-115534**

Date	Description	Amount	Status
10-26-16	COP 2: Removal of 700 lf of asbestos containing TSI material. Contractor to provide additional documents. Per District's direction, the cost will be processed as an allowance adjustment.	\$37,597.62	ACO-1 to Contractor
02-22-17	COP 3: Removal and disposal of Owner contents and demolish plaster ceilings in kitchen at Owner's request. This cost is an allowance adjustment per the Owner.	\$12,280.66	ACO-1 to Contractor
02-22-17	COP 4: Removal and disposal of Owner contents from Dressing Rooms at Owner's request. This cost is an allowance adjustment per the Owner.	\$15,396.25	ACO-1 to Contractor

CHANGE ORDER PROPOSAL LOG
Mod. A#03-115534

Date	Description	Amount	Status
02-22-17	COP 5: Owner requested underground utility locating.	\$3,570.51	ACO-1 to Contractor
03-06-17	COP 6: Deletion of Cast Stone scope per Owner request.	-\$65,000.00	Create CO per District Direction
03-06-17	COP 7: Changes to door hardware. Per Owner request.	\$2,954.49	Create CO per District Direction
03-06-17	COP 8: Owner requested underground utility locating.	\$2,031.28	ACO-1 to Contractor
03-06-17	COP 9: Water jet existing storm drain and create video of existing storm drain line at the Owner's request.	\$4,213.96	ACO-1 to Contractor
05-01-17	COP 10: Per District's request, install (2) 4" PVC conduits from underground vault at Mustang Café to Building E.	\$7,443.23	Create CO per District Direction
05-01-17	COP 11: Intercept existing VCP sewer line and reroute approx. 200 LF to a manhole south of Buildings B and E.	\$18,373.13	ACO-1 to Contractor
05-15-17	COP 12: Provide new theatre seating in lieu of renovating existing seating per the Contract Documents per the District's request.	\$95,220.00	Pending Submittal Approval
05-15-17	COP 13: Partial demolition necessary for structural steel installation per PR-04.	\$48,296.54	Create CO per District Direction
07-04-17	COP 14: Replace existing 6" fire line from Lincoln to the north side of the Mustang Café (RFI 056).	\$152,724.55	Pending District Direction
07-10-17	COP 15: Additional abatement in cafeteria.	\$21,375.13	ACO-1 to Contractor
07-10-17	COP 16: Replace existing fire sprinkler piping (RFI 077 & 077R1).	\$53,620.76	Create CO per District Direction
07-17-17	COP 17: Owner requested revisions to specified A/V system.	\$62,978.39	Create CO per District Direction

**CHANGE ORDER PROPOSAL LOG
 Mod. A#03-115534**

Date	Description	Amount	Status
07-17-17	COP 18: Optional Owner requested A/V equipment.	\$31,359.95	Create CO per District Direction
07-25-17	COP 19: Owner requested refinishing of existing wood gym flooring.	\$49,765.11	Create CO per District Direction
09-06-17	COP 20R1: Owner requested revisions to the new center court logo in the gym.	\$10,074.40	Pending District approval
09-05-17	COP 21: Cost to provide FRP panels at the kitchen in lieu of paint per the Owner's request.	\$18,329.00	Pending District approval
09-19-17	COP 22R1: Cost for storm drain revisions per the District's request.	\$127,555.26	Pending District review

ALLOWANCE CONTINGENCY LOG (For All 3 projects)

Date	Description	Amount	Remaining	Status
10-26-16	COP 2: Removal of 700 lf of asbestos containing TSI material. Contractor to provide additional documents. Per District's direction, the cost will be processed as an allowance adjustment.	\$37,597.62	\$262,402.38	ACO-1 to Contractor
02-22-17	COP 3: Removal and disposal of Owner contents and demolish plaster ceilings in kitchen.	\$12,280.66	\$250,121.72	ACO-1 to Contractor
02-22-17	COP 4: Removal and disposal of Owner contents from Dressing Rooms.	\$15,396.25	\$234,725.47	ACO-1 to Contractor
07-10-17	COP 15: Additional abatement in cafeteria.	\$21,375.13	\$213,350.34	ACO-1 to Contractor
02-22-17	COP 5: Owner requested underground utility locating.	\$3,570.51	\$209,779.83	ACO-1 to Contractor
03-06-17	COP 8: Owner requested underground utility locating.	\$2,031.28	\$207,748.55	ACO-1 to Contractor
03-06-17	COP 9: Water jet existing storm drain and create video of existing storm drain line at the Owner's request.	\$4,213.96	\$203,534.59	ACO-1 to Contractor

ALLOWANCE CONTINGENCY LOG (For All 3 projects)

Date	Description	Amount	Remaining	Status
05-01-17	COP 11: Intercept existing VCP sewer line and reroute approximately 200 LF to a manhole south of Buildings B and E.	\$18,373.13	\$185,161.46	ACO-1 to Contractor

**CONSTRUCTION CHANGE DOCUMENTS (CCD) LOG - CATEGORY A
Mod. A#03-115534**

No.	Description	Status
001	Revise guardrail and eliminate horse profile at quad area (VE item).	Approved 12/15/16
002	Provide T-bar ceilings in lieu of framed hard lid ceilings at first and second floor foyers (VE item).	Approved 12/15/16
003	Eliminate free-standing concrete monuments in quad area (VE item).	Approved 12/15/16
004	Eliminate all Senior Courtyard work at Building A (VE item).	Approved 02/01/17
005	Additional information for new framing at existing Theatre side walls and soffits.	Approved 02/22/17
006	Remove cast stone scope.	Approved 03/09/17
007	Replace fire sprinkler pipes at existing Cafeteria.	Approved 06/13/17
008	Revisions to metal framing at niches and house left and right stage walls.	Submitted to DSA 08-28-17
009	Revision of structural support for new speaker arrays (pending District approval of redesign fees).	District to Approve Fee
010	Connection of HSS columns to existing concrete pilasters.	Approved 09/22/17

**CONSTRUCTION CHANGE DOCUMENTS (CCD) LOG - CATEGORY B
Mod. A#03-115534**

No.	Description	Status
001	Eliminate wood finish at Auditorium and first floor foyer. Revise finishes (VE item).	Issued 02-05-16
002	Eliminate (4) chandelier fixtures from Auditorium scope (VE item).	Issued 12-05-16
003	Revise conduit size from 1" to 3/4" at A/V device back boxes.	Issued 03-29-17

CONSTRUCTION CHANGE DOCUMENTS (CCD) LOG – CATEGORY B
Kitchen A#03-115819

No.	Description	Status
001	Revisions to electrical and low voltage.	Issued 03-13-17
002	Per District's request, provide new walk-in refrigerator. Refer to PR2.	Issued 06-09-17

SUBMITTAL LOG

SEE ATTACHED LOG

PROPOSAL REQUEST LOG
Mod. A#03-115534

No.	Description	Status
001	Storm drain revision.	Issued 07-13-17 COP 22: 09-19-17
002	Conduit size change for security surveillance camera system.	Issued 03-29-17
003	Spare (2) 4" conduit from existing pull box north of Building B to Building E.	COP 10: 05-01-17
004	Obstructions with steel columns and beams installation.	Issued 05-8-17 COP 13: 05-15-17
005	Replace existing bent and damaged fire sprinkler pipes at the cafeteria.	Issued 05-15-17 COP 16: 07-10-17

PROPOSAL REQUEST LOG
Kitchen A#03-115819

No.	Description	Status
001	Various electrical clarifications.	Issued 03-10-17
002	Per District's request, provide new walk-in refrigerator.	Issued 06-09-17

REQUEST FOR INFORMATION LOG

SEE ATTACHED LOG

PAYMENT APPLICATIONS LOG
Mod. A#03-115534

No.	Date Rec.	Description	Status
001	10-25-16	October, 2016	Warrant issued
		No request for November, 2016	N/A
002	01-03-17	December draft received January 3, 2017	Warrant issued
		No request received for January, 2017	N/A
		No request received for February, 2017	N/A
003	04-11-17	Pay request 003 (Zero dollar pay request)	Warrant issued
004	04-11-17	March pay request	Warrant issued
005	05-16-17	April pay request	Warrant issued
		No request received for May, 2017	N/A
006	07-11-17	June pay request	Warrant issued
		No request received for July, 2017	N/A
007	08-29-17	August request	Warrant issued
	10-03-17	No request received for September, 2017	N/A

ACTION ITEMS

1. The **District's A/V consultant** provided new A/V equipment requirements for the theatre project. Checkpoint provided a cost summary to the Contractor for their use in creating a COP for District consideration. Contractor issued an RFI regarding whether the originally designed structure will support the additional weight of the proposed speakers. An RFI was received August 4, 2017. The District directed the Architect to have the Structural Engineer redesign the support structure to accommodate the proposed speaker arrays and submit the additional design fees to the District. The proposal was forwarded to the District August 8, 2017, for review and a verbal approval was provided by the District. Board approval to follow. The **District** is reviewing the A/V equipment internally. On October 3, 2017, the District stated that they would like to add two video monitors to the dressing rooms.
2. The Architect made another request to the **Contractor** for all submittals. All submittals were due no later than 35 days of receiving the Notice to Proceed. Outstanding submittals are critically late and may affect the project schedule. **The District made a request for all outstanding submittals.** The Architect shared the updated Contractor submittal schedule during the meeting. The District stated that some of the submittal requirements are not relevant and can be removed from the Contractor's submittal schedule.

3. On July 11, 2017, the District requested a cost delta from the Contractor to provide FRP panels at the Kitchen walls in lieu of paint. The COP was received September 12, 2017 and is under review by the District. The **District** is consulting with their food services director regarding the decision to move forward with the proposed FRP panels. As of October 3, 2017, no direction has been provided.
4. On June 27, 2017, the Contractor proposed an alternate design at the four new door openings at the north side of the cafeteria in lieu of the RFI 053 response. The proposal is to saw cut down from the original window openings on both sides of each opening and adding side panels to the door framing in lieu of infilling the existing concrete openings and reframing of the existing walls. The District requested a cost delta from the **Contractor** for review. The District did state that any additional costs would be an item of concern. As of October 3, 2017, a cost proposal has not been received.
5. On August 15, 2017, the Architect requested a revised project schedule from the **Contractor** for review at the next meeting. A revised project schedule was not provided as requested. The Contractor stated they would provide the revised project schedule at the August 29, 2017 meeting. An updated schedule was submitted by the Contractor on September 12, 2017 showing an extended project end date. The **Contractor** will e-mail the schedule to the team. The electronic version of the schedule has not been received as of September 26, 2017. A hard copy of the schedule was provided on October 3, 2017 and is attached.
6. The P.I. feels that due to the number of fire sprinkler field changes in the cafeteria area, the creation of a CCD-A may be necessary. The **Architect** will review the changes and advise.
7. The District requested the **Contractor** contact the bleacher manufacturer regarding the possibility of permanently removing the back row of seats to reduce the new bleacher overall projection into the gym space. No information provided as of this meeting date.

INFORMATION ITEMS/CALENDAR

1. The Principal stated that winter break will begin December 21, 2017 with students returning January 8, 2018.

NEXT JOB MEETING: 8:30 a.m., Tuesday, October 10, 2017.

The foregoing shall be considered as confirmed unless clarification or amendment is received by this Office within ten (10) calendar days.

ARCHITECT'S SITE OBSERVATION NOTICE

The Contractor shall supervise and direct the work. The Contractor shall be solely responsible for and have exclusive control over construction safety, means, methods, techniques, sequences, procedures, temporary facilities and controls, and for coordinating all portions of the Work. The Contractor shall be responsible for inspection of portions of the Work already performed to determine that such portions are in proper condition to receive subsequent Work. The Contractor shall not be relieved of any obligation to perform the Work in accordance with the Contract Documents by any action or duty of the Architect. The Architect, as a representative of the Owner, will determine in general if the Work is being performed in a manner that would indicate that the Work, when fully completed, will be in accordance with the Contract Documents. The Architect will not be responsible for the Contractor's failure to perform the Work in accordance with the Contract Documents. The Architect will not make exhaustive or continuous on-site inspections to check the quality or quantity of the Work and will not have control over or charge of, nor be responsible for, coordinating the Work, construction means, methods, techniques, sequences, procedures, temporary facilities and controls or for safety precautions and programs in connection with the Work.

Prepared by:



DARYL VAN DRAN
Project Manager

DV:gs/P5091390044-fr

Attached: Submittal Log
 RFI Log
 Contractor's Revised Schedule



ARCHITECTS CLIENT FOCUSED. PASSION DRIVEN.

SUBMITTAL LOG - PRODUCT DATA, SHOP DRAWINGS AND SAMPLES

John Muir High School Modernization

Pasadena Unified School District

The Nazerian Group

Contractor:

N/A

Construction Manager:

Project No.: 0913900

Action Legend

- 1 = Review Completed, Do Not Resubmit
- 2 = Revise as Noted, Do Not Resubmit
- 3 = Revise as Noted, Resubmit for Record
- 4 = Not Acceptable, Make New Submittal

SUBMITTAL NO.	DATE RECEIVED	SPECIFICATION SECTION	TITLE / DESCRIPTION	CONTRACTOR / SUBCONTRACTOR / TRADE	QUANTITY RECEIVED			REFERRED			ACTION (Legend Above)	COPIES TO								
					PRODUCT DATA	SHOP DWGS	SAMPLES	TO	DATE SENT	COPIES SENT		DATE RETD	DATE RETURNED	CONTRACTOR	OWNER	INSPECTOR	ARCHITECT	CONSULTANT		
01	10/18/16	GCs	Schedule of Values	Nazerian	1				-	-	-	4	10/21/16	1	1	1	1			
01A	10/25/16	GCs	Schedule of Values resubmittal (approved by PUSD)	Nazerian	1				-	-	-	1	10/25/16	1	1	1	1			
02	11/07/16	01310	Project Schedule	Nazerian	1				PUSD	11/07/16	e	4	11/15/16	1	1	1	1			
02A	02/07/17	01310	Project Schedule (accepted by PUSD as a baseline, revisions are req'd)	Nazerian	1				PUSD	02/07/17	e	2	02/08/17	1	1	1	1			
001	12/21/16	126613	Telescopic Bleachers (deferred approval)	Nazerian/Hussey	3				DSA	01/09/17	2	4	02/14/17	1	1	1	1			
001	04/11/17	126613	Telescopic Bleachers (deferred approval) resubmittal OTC	Nazerian/Hussey	3				DSA	04/14/17	1	1	04/18/17	1	1	1	1			
001	12/21/16	126613	Telescopic Bleachers (deferred approval)	Nazerian/Hussey	3				DCGA	01/04/17	e	1	02/14/17	1	1	1	1			
001A	04/25/17	126613	Telescopic Bleachers (deferred approval)	Nazerian/Hussey	3				DCGA	04/25/17	e	1	05/03/17	1	1	1	1			
001B	05/11/17	126613	Telescopic Bleachers (Graphic Logo)	Nazerian/Hussey	1				-	-	e	1	05/17/17	1	1	1	1			
002	12/21/16	09649	Wood Stage Flooring	Nazerian/HUR	1	2			-	-	e	1&2	01/03/17	1	1	1	1			
003	12/21/16	10400	Identifying Devices (no samples rec'vd)	Nazerian/Kendall Sign	1	1			-	-	e	4	01/30/17	1	1	1	1			
003A	02/10/17	10400	Identifying Devices - Substitution Request	Nazerian/Kendall Sign	1				-	-	e	4	02/14/17	1	1	1	1			
003B	02/15/17	10400	Identifying Devices - Substitution Request	Nazerian/Kendall Sign	1				-	-	e	4	02/23/17	1	1	1	1			
003C	08/22/17	10400	Identifying Devices - Substitution Request samples only	Nazerian/Kendall Sign	1				-	-	e									
004	12/21/16	08210	Wood Doors (no samples rec'vd)	Nazerian/ADA	1				-	-	e	4	01/30/17	1	1	1	1			
004A	07/11/17	08210	Wood Door samples	Nazerian	1				-	-	e	1	07/31/17	1						
005	12/21/16	08110	Steel Doors and Frames (no samples rec'vd)	Nazerian/ADA	1	1			-	-	e	3	03/13/17	1	1	1	1			
005A	05/10/17	08110	Steel Doors and Frames (no samples rec'vd)	Nazerian/ADA	1	1			-	-	e	2	05/22/17	1	1	1	1			
006	12/21/16	08710	Door Hardware	Nazerian/ADA	1				AHS	01/25/17	e	3	02/13/17	1	1	1	1			
007	12/29/16	05120	Structural Steel (electronic bolt and shop drawings)	Nazerian/Columbia	1				RM Byrd	01/06/17	e	4	01/06/17	1	1	1	1			

SUBMITTAL LOG - PRODUCT DATA, SHOP DRAWINGS AND SAMPLES

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.: 0913900

Action Legend

- 1 = Review Completed, Do Not Resubmit
- 2 = Revise as Noted, Do Not Resubmit
- 3 = Revise as Noted, Resubmit for Record
- 4 = Not Acceptable, Make New Submittal

SUBMITTAL NO.	DATE RECEIVED	SPECIFICATION SECTION	TITLE / DESCRIPTION	CONTRACTOR / SUBCONTRACTOR / TRADE	QUANTITY RECEIVED			REFERRED				DATE RETURNED	COPIES TO					
					PRODUCT DATA	SHOP DWGS	SAMPLES	TO	DATE SENT	COPIES SENT	DATE RET'D		ACTION (Legend Above)	CONTRACTOR	OWNER	INSPECTOR	ARCHITECT	CONSULTANT
007A	01/13/17	05120	Structural Steel (hard copy bolt and shop drawings)	Nazerian/Columbia		3			RM Byrd	01/16/17	e	02/02/17	1,2	1	1	1	1	1
007B	02/03/17	05120	Additional Structural Steel Drawings not previously reviewed	Nazerian/Columbia		3			RM Byrd	02/06/17	e	02/15/17	1,2	1	1	1	1	1
007C	08/04/17	05120	Structural Steel (welding procedures)	Nazerian/Columbia	1				RM Byrd	08/04/17	e	08/04/17	1	1	1	1	1	1
008	01/04/17	15900	Energy Management System	Nazerian/Schneider	1				CEDG	01/04/17	e	01/30/17	2	1	1	1	1	1
009	01/24/17	09331	Quarry Tile Floor Finish (gray color)	Nazerian/JNJ	1		2		-	-	e	-	2	1	1	1	1	1
010	02/03/17	05520	Handrails and Railings	Nazerian/Columbia		3			RM Byrd	02/06/17	3	02/15/17	1,2	1	1	1	1	1
011	02/10/17	03300	Concrete Mix Design	Nazerian/Robertsons	1				MSL/RM Byrd	02/10/17	e	02/15/17	2	1	1	1	1	1
011A	02/28/17	03300	Concrete Mix Design (1-page SOG Info)	Nazerian/Robertsons	1				RM Byrd	03/02/17	e	03/02/17	2	1	1	1	1	1
012	02/22/17	09111	Metal Stud Framing System	Nazerian/Schmitt	1				-	-	e	-	2	1	1	1	1	1
012A	04/26/17	09111	Metal Stud Framing System (Titen anchors)	Nazerian/Schmitt	1				RM Byrd	05/03/17	e	05/03/17	1	1	1	1	1	1
013	02/22/17	09260	Gypsum Board Systems	Nazerian/Schmitt	1				-	-	e	-	2	1	1	1	1	1
014	02/22/17	09216	Gypsum Board Assemblies	Nazerian/Schmitt	1				-	-	e	-	2	1	1	1	1	1
015	02/21/17	11400	Food Service Equipment VE items	Nazerian/Kitcor	2				L & S	02/21/17	e	03/22/17	2	1	1	1	1	1
015A	02/23/17	11400	Food Service Equipment	Nazerian/Kitcor	1				L & S	02/24/17	e	03/20/17	1	1	1	1	1	1
015B	02/24/17	11400	Food Service Equipment (Shop Drawings)	Nazerian/Kitcor	1				L & S	02/27/17	e	03/20/17	3	1	1	1	1	1
015C	03/10/17	11400	Food Service Equipment (Refrigeration Shops)	Nazerian/Omni	1				L & S	03/10/17	e	03/20/17	1	1	1	1	1	1
015D	03/20/17	11400	Food Service Equipment (Walk-in Ref Shops)	Nazerian/Thermalrite	1				L & S	03/21/17	e	03/21/17	3	1	1	1	1	1
015E	05/10/17	11400	Food Service Equipment	Nazerian/Kitcor	1				L & S	05/10/17	e	05/17/17	1	1	1	1	1	1
015F	05/10/17	11400	Food Service Equipment (Walk-in Ref Shops)	Nazerian/Kitcor	1				L & S	05/10/17	e	05/17/17	1	1	1	1	1	1
015G	05/10/17	11400	Food Service Equipment	Nazerian/Kitcor	1				L & S	05/10/17	e	05/17/17	1	1	1	1	1	1
015H	05/10/17	11400	Food Service Equipment (Color Chart)	Nazerian/Kitcor	1			1	L & S	05/10/17	e	05/23/17	2	1	1	1	1	1
015I	05/10/17	11400	Food Service Equipment (Locker Color Chart)	Nazerian/Kitcor	1			1	L & S	05/10/17	e	05/23/17	2	1	1	1	1	1
016	02/27/17	02530	Sanitary Sewerage	Nazerian	1				MSL	02/27/17	e	03/13/17	2	1	1	1	1	1
017	03/03/17	09240	Cement Plastering (Kitchen scope)	Nazerian/Schmitt	1				-	-	e	-	3	1	1	1	1	1
017A	07/05/17	09240	Cement Plastering (Kitchen scope) (plaster material only)	Nazerian/Schmitt	1				-	-	e	-	1	1	1	1	1	1
018	03/06/17	16111	Conduit	Nazerian	1				DCGA	03/07/17	e	03/09/17	4	1	1	1	1	1
018A	03/10/17	16111	Conduit	Nazerian	1				DCGA	03/10/17	e	03/15/17	1	1	1	1	1	1
019	03/08/17	02554	Natural Gas Distribution	Nazerian	1				CEDG	03/08/17	e	03/10/17	1	1	1	1	1	1
020	03/08/17	02630	Storm Drainage	Nazerian	1				MSL	03/08/17	e	03/13/17	2	1	1	1	1	1

SUBMITTAL LOG - PRODUCT DATA, SHOP DRAWINGS AND SAMPLES

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.: 0913900

Action Legend

- 1 = Review Completed, Do Not Resubmit
- 2 = Revise as Noted, Do Not Resubmit
- 3 = Revise as Noted, Resubmit for Record
- 4 = Not Acceptable, Make New Submittal

SUBMITTAL NO.	DATE RECEIVED	SPECIFICATION SECTION	TITLE / DESCRIPTION	CONTRACTOR / SUBCONTRACTOR / TRADE	QUANTITY RECEIVED			REFERRED				DATE RETURNED	COPIES TO						
					PRODUCT DATA	SHOP DWGS	SAMPLES	TO	DATE SENT	COPIES SENT	DATE RET'D		ACTION (Legend Above)	CONTRACTOR	OWNER	INSPECTOR	ARCHITECT	CONSULTANT	
020A	05/15/17	02630	Storm Drainage	Nazerian	1			MSL	05/15/17	e	05/23/17	1	1	1	1	1	1	1	1
021	03/10/17	15160	Vibration, Isolation & Seismic Restraints	Nazerian/Sigler	1			CEDG	03/10/17	e	03/24/17	4	1	1	1	1	1	1	1
022	03/10/17	15700	Wet Heat Transfer	Nazerian/Sigler	1			CEDG	03/10/17	e	03/15/17	4	1	1	1	1	1	1	1
022A	06/01/17	15700	Wet Heat Transfer (resubmittal)	Nazerian	1			CEDG	06/01/17	e	06/09/17	1	1	1	1	1	1	1	1
022B	06/01/17	15700	Wet Heat Transfer	Nazerian	1			CEDG	06/01/17	e	06/09/17	4	1	1	1	1	1	1	1
022C	06/12/17	15700	Wet Heat Transfer	Nazerian	1			CEDG	06/12/17	e	06/13/17	4	1	1	1	1	1	1	1
022D	06/12/17	15700	Wet Heat Transfer	Nazerian	1			CEDG	06/12/17	e	06/13/17	2	1	1	1	1	1	1	1
022E	06/23/17	15700	Wet Heat Transfer	Nazerian	1			CEDG	06/23/17	e	06/29/17	4	1	1	1	1	1	1	1
022F	08/04/17	15700	Wet Heat Transfer	Nazerian/ADS	1			CEDG	08/07/17	e	08/11/17	1.3	1	1	1	1	1	1	1
022G	09/11/17	15700	Wet Heat Transfer	Nazerian/ADS	1			CEDG	09/11/17	e	09/12/17	1	1	1	1	1	1	1	1
023A	03/15/17	15800	Air Conditioning and Air Handling Equipment (additional product data)	Nazerian	1			CEDG	03/20/17	e	03/23/17	1.3	1	1	1	1	1	1	1
023B	03/20/17	15800	Air Conditioning and Air Handling Equipment (additional product data)(air curtain)	Nazerian	1			CEDG	03/20/17	e	03/30/17	1	1	1	1	1	1	1	1
023C	06/23/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/Sigler	1			CEDG	06/23/17	e	06/29/17	1	1	1	1	1	1	1	1
023D	06/23/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/Sigler	1	1		CEDG	06/23/17	e	07/05/17	3	1	1	1	1	1	1	1
023E	06/23/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/Sigler	1	1		CEDG	06/23/17	e	07/05/17	3	1	1	1	1	1	1	1
023F	07/24/17	15800	AC and AH EQ. (non insulated roof curbs)	Nazerian/DMG	1			CEDG/Bryd	07/24/17	e	07/25/17	1	1	1	1	1	1	1	1
023G	07/24/17	15800	Air Conditioning and Air Handling Equipment	Nazerian	1			CEDG	07/24/17	e	08/01/17	1	1	1	1	1	1	1	1
023H	08/03/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/DMG	1			CEDG	08/03/17	e	08/04/17	1	1	1	1	1	1	1	1
023I	08/16/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/DMG	1			CEDG	08/16/17	e	08/18/17	1,2,3	1	1	1	1	1	1	1
023J	09/21/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/DMG	1			CEDG	09/21/17	e	09/27/17	3	1	1	1	1	1	1	1
023K	10/06/17	15800	Air Conditioning and Air Handling Equipment	Nazerian/DMG	1			CEDG		e									
024A	03/15/17	15840	Air Transmission and Distribution System (additional product data)	Nazerian/Air Design	1			CEDG	03/20/17	e	03/23/17	3	1	1	1	1	1	1	1
024B	03/20/17	15840	Air Transmission and Distribution System (additional product data)(dampers)	Nazerian/Air Design	1			CEDG	03/20/17	e	03/30/17	1	1	1	1	1	1	1	1
025	03/10/17	15890	Sound Attenuators	Nazerian	1			CEDG	03/10/17	e	03/13/17	1	1	1	1	1	1	1	1
025A	06/02/17	15890	Sound Attenuators	Nazerian	1			CEDG	06/02/17	e	06/06/17	1	1	1	1	1	1	1	1
026	03/10/17	07840	Firestopping	Nazerian	1			-	-	e	-	1	1	1	1	1	1	1	1
027	03/10/17	16123	Bldg Wire and Cable	Nazerian	1			DCGA	03/10/17	e	03/15/17	3	1	1	1	1	1	1	1

SUBMITTAL LOG - PRODUCT DATA, SHOP DRAWINGS AND SAMPLES

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.: 0913900

Action Legend

- 1 = Review Completed, Do Not Resubmit
- 2 = Revise as Noted, Do Not Resubmit
- 3 = Revise as Noted, Resubmit for Record
- 4 = Not Acceptable, Make New Submittal

SUBMITTAL NO.	DATE RECEIVED	SPECIFICATION SECTION	TITLE / DESCRIPTION	CONTRACTOR / SUBCONTRACTOR / TRADE	QUANTITY RECEIVED			REFERRED				ACTION (Legend Above)	DATE RETURNED	COPIES TO			
					PRODUCT DATA	SHOP DWGS	SAMPLES	TO	DATE SENT	COPIES SENT	DATE RET'D			CONTRACTOR	OWNER	INSPECTOR	ARCHITECT
027A	06/13/17	16123	Bldg Wire and Cable	Nazerian	1			DCGA	06/19/17	e	06/21/17	2	1	1	1	1	1
028	03/10/17	16141	Wiring Devices	Nazerian	1			DCGA	03/10/17	e	03/15/17	3	1	1	1	1	1
029	03/10/17	16170	Grounding and Bonding	Nazerian	1			DCGA	03/10/17	e	03/15/17	3	1	1	1	1	1
029A	04/25/17	16170	Grounding and Bonding	Nazerian	1			DCGA	04/25/17	e	04/26/17	2	1	1	1	1	1
030	03/10/17	16529	Hangers and Supports Electrical	Nazerian	1			DCGA	03/10/17	e	04/03/17	4	1	1	1	1	1
031	03/10/17	16130	Boxes	Nazerian	1			DCGA	03/10/17	e	03/15/17	3	1	1	1	1	1
031A	04/25/17	16130	Boxes	Nazerian	1			DCGA	04/25/17	e	04/26/17	3	1	1	1	1	1
031B	04/27/17	16130	Boxes (no octagonal boxes)	Nazerian	1			DCGA	04/28/17	e	05/03/17	2	1	1	1	1	1
032	03/15/17	15030	Identification	Nazerian	1			-	-	e	-	4	1	1	1	1	1
033	03/15/17	15050	Basic Materials and Methods	Nazerian	1			CEDG	03/20/17	e	03/23/17	4	1	1	1	1	1
034	04/14/17	11065	Theatrical Stage Rigging & Drapery Equip (Drapery color selection by Architect)	Protech/Nazerian	1			Ruzika	04/14/17	e	05/03/17	3	1	1	1	1	1
034A	06/02/17	11065	Theatrical Stage Rigging & Drapery Equip (Drapery color selection by Architect)	Protech/Nazerian	1			Ruzika	06/02/17	e	06/28/17	1	1	1	1	1	1
035	05/10/17	03200	Concrete Reinforcement	Nazerian	1			RM Byrd	05/10/17	e	05/16/17	2	1	1	1	1	1
035A	05/30/17	03200	Concrete Reinforcement	Nazerian	1			RM Byrd	05/31/17	e	05/31/17	1	1	1	1	1	1
036	03/15/17	15180	Insulation	Nazerian	1			CEDG	03/20/17	e	03/23/17	3	1	1	1	1	1
037	04/24/17	02510	Water Distribution	Nazerian	1			MSL	04/24/17	e	05/01/17	2	1	1	1	1	1
038	04/24/17	16511	Interior Lighting	Nazerian	1			DCGA	04/24/17	e	04/25/17	3	1	1	1	1	1
038A	05/10/17	16511	Interior Lighting	Nazerian	1			DCGA	05/10/17	e	05/11/17	2,3	1	1	1	1	1
038B	06/19/17	16511	Interior Lighting	Nazerian	1			DCGA	06/19/17	e	06/21/17	1,2,3	1	1	1	1	1
038C	07/11/17	16511	Interior Lighting	Nazerian	1			DCGA	06/19/17	e	07/11/17	3	1	1	1	1	1
038D	07/24/17	16511	Interior Lighting	Nazerian	1			DCGA	07/24/17	e	07/27/17	3	1	1	1	1	1
038E	08/08/17	16511	Interior Lighting	Nazerian	1			DCGA/Ruzika	08/08/17	e	08/28/17	2	1	1	1	1	1
038F	08/08/17	16511	Interior Lighting (gym photometrics)	Nazerian	1			DCGA	08/08/17	e	08/14/17	1	1	1	1	1	1
038G	08/16/17	16511	Interior Lighting	Nazerian	1			DCGA	09/27/17	e	09/27/17	2	1	1	1	1	1
038H	08/18/17	16511	Interior Lighting	Nazerian	1			DCGA	08/08/17	e	09/12/17	2	1	1	1	1	1
038I	09/07/17	16511	Interior Lighting (and photometrics)	Nazerian	1			DCGA	08/08/17	e	09/12/17	1-2-3	1	1	1	1	1
038J	09/27/17	16511	Interior Lighting	Nazerian	1			DCGA	09/07/17	e	09/12/17	2-3	1	1	1	1	1
039	04/25/17	16160	Cabinets and Enclosures	Nazerian	1			DCGA	09/28/17	e	09/28/17	1	1	1	1	1	1
040	03/15/17	15020	Equipment and Systems Tests	Nazerian / SOCAL	1			CEDG	03/20/17	e	03/23/17	2,4	1	1	1	1	1

SUBMITTAL LOG - PRODUCT DATA, SHOP DRAWINGS AND SAMPLES

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.: 0913900

Action Legend

- 1 = Revise as Noted, Do Not Resubmit
- 2 = Revise as Noted, Do Not Resubmit
- 3 = Revise as Noted, Resubmit for Record
- 4 = Not Acceptable, Make New Submittal

SUBMITTAL NO.	DATE RECEIVED	SPECIFICATION SECTION	TITLE / DESCRIPTION	CONTRACTOR / SUBCONTRACTOR / TRADE	QUANTITY RECEIVED			REFERRED				DATE RETURNED	COPIES TO				
					PRODUCT DATA	SHOP DWGS	SAMPLES	TO	DATE SENT	COPIES SENT	DATE RET'D		ACTION (Legend Above)	CONTRACTOR	OWNER	INSPECTOR	ARCHITECT
041	03/17/17	16470 16413	Panelboards Switchboards	Nazerian	1			DCGA	03/20/17	e	03/22/17	4	1	1	1	1	1
041A	04/17/17	16470 16413	Panelboards Switchboards (substitution request)	Nazerian	1			PUSD	05/02/17	e	05/02/17	4	1	1	1	1	1
041B	06/19/17	16470 16413	Panelboards Switchboards (substitution request)	Nazerian	1			DCGA	06/21/17	e	06/27/17	1,2,3,4	1	1	1	1	1
041C	07/17/17	16470 16413	Panelboards Switchboards (substitution request)	Nazerian	1			DCGA	07/17/17	e	07/18/17	2	1	1	1	1	1
041D	07/25/17	16470 16413	Panelboards Switchboards (substitution request)	Nazerian	1			DCGA	07/25/17	e	07/27/17	2	1	1	1	1	1
042	03/20/17	15840	Air Trans and Distr System shop drawings	Nazerian/Air Design	1			CEDG	03/20/17	e	03/31/17	4	1	1	1	1	1
043	04/26/17	15420 220020	Domestic & Industrial Water System Mod. And Kitchen	Nazerian	1			CEDG	04/28/17	e	04/28/17	1	1	1	1	1	1
044	05/27/17	16580	Theatrical Lighting & Stage Equipment	Nazerian	1			Ruzika	05/27/17	e	06/01/17	4	1	1	1	1	1
044A	06/06/17	16580	Theatrical Lighting & Stage Equipment	Nazerian	1			Ruzika	06/06/17	e	06/27/17	3	1	1	1	1	1
044B	07/24/17	16580	Theatrical Lighting & Stage Equipment	Nazerian	1			Ruzika	07/24/17	e	08/08/17	2	1	1	1	1	1
045	03/20/17	10210	Wall Louvers	Nazerian	1			-	-	e	-	2	1	1	1	1	1
046	05/11/17	09900	Painting	Nazerian	1			-	-	e	-	1	1	1	1	1	1
047	05/11/17	09511	Suspended Acoustical Ceilings (No samples)	Nazerian	1			-	-	e	-	1	1	1	1	1	1
047	06/06/17	09511	Suspended Acoustical Ceilings (samples)	Nazerian	1			-	-	e	-	1	1	1	1	1	1
048	05/11/17	16721	Intelligent Fire Detection & Alarm System	Nazerian	1			DCGA	05/11/17	e	05/17/17	4	1	1	1	1	1
048A	06/02/17	16721	Intelligent Fire Detection & Alarm (Letter)	Nazerian	1			DCGA	05/11/17	e	06/02/17	4	1	1	1	1	1
049	06/02/17	09840	Fabric Wrapped Acoustical Panels (PD & Shops)	Nazerian	1			-	-	e	-	1	1	1	1	1	1
049	06/06/17	09840	Fabric Wrapped Acoustical Panels (Samples)	Nazerian	1			-	-	e	-	2	1	1	1	1	1
050	06/16/17	13915	Wet Pipe-Suppression Sprinklers	Nazerian/APEX	1			IMEG	06/16/17	e	06/19/17	1	1	1	1	1	1
051	06/27/17	15470	Plumbing fixtures	Nazerian	1			CEDG	06/27/17	e	06/28/17	1	1	1	1	1	1
051A	06/27/17	15470	Plumbing fixtures	Nazerian	1			CEDG	06/27/17	e	06/28/17	2	1	1	1	1	1
051B	06/27/17	15470	Plumbing fixtures	Nazerian	1			L & S	06/27/17	e	07/10/17	2	1	1	1	1	1
052	07/25/17	12611	Theater Seating Renovation	Nazerian	1			-	-	e	-	4	1	1	1	1	1

SUBMITTAL LOG - PRODUCT DATA, SHOP DRAWINGS AND SAMPLES

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.: 0913900

Action Legend

- 1 = Review Completed, Do Not Resubmit
- 2 = Revise as Noted, Do Not Resubmit
- 3 = Revise as Noted, Resubmit for Record
- 4 = Not Acceptable, Make New Submittal

SUBMITTAL NO.	DATE RECEIVED	SPECIFICATION SECTION	TITLE / DESCRIPTION	CONTRACTOR / SUBCONTRACTOR / TRADE	QUANTITY RECEIVED			REFERRED				ACTION (Legend Above)	DATE RETURNED	COPIES TO										
					PRODUCT DATA	SHOP DWGS	SAMPLES	TO	DATE SENT	COPIES SENT	DATE RET'D			CONTRACTOR	OWNER	INSPECTOR	ARCHITECT	CONSULTANT						
052A	10/02/17	12611	Theater Seating Renovation	Nazerian/Herk Edwards	1																			
053	07/25/17	16461	Dry Type Transformers	Nazerian	1			07/25/17		e		07/27/17		2	07/27/17	1	1	1	1	1	1	1	1	1
054	07/25/17	16440	Load Interrupter Switch	Nazerian	1			07/25/17		e		07/27/17		1	07/27/17	1	1	1	1	1	1	1	1	1
055	08/10/17	16770	Audio Visual Equipment (shop drawings)	Nazerian/Checkpoint District reviewing	1			08/10/17	MLA/DCGA/Ruzika	e														
056	08/16/17	15190	Electric motors and var. freq. drives	Nazerian/DMG	1			08/16/17	CEDG	e		08/17/17		4	08/18/17	1	1	1	1	1	1	1	1	1
057	09/06/17	10520	Fire Protection Specialties	Nazerian	1			-	-	e				4	09/12/17	1	1	1	1	1	1	1	1	1
058	09/19/17	08333	Overhead Coiling Door	Nazerian	1			09/19/17	DCGA	e		09/19/17		1	09/20/17	1	1	1	1	1	1	1	1	1
058A	09/26/17	08333	Overhead Coiling Door (color chart)	Nazerian	1				-															



ARCHITECTS CLIENT FOCUSED. PASSION DRIVEN.

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
001	09/29/16	Theater Seating Questions	-	-	-	10/04/16
002	10/19/16	Unforseen Asbestos in ceiling	-	-	-	10/20/16
002R	10/21/16	added info for above question	CEDG	10/21/16	10/24/16	10/25/16
003	12/09/16	Unknown existing sewer questions (provide info)	MSL	12/09/16	12/12/16	12/13/16
004	12/09/16	Compaction percentage requirement	MSL/RM Byrd	12/09/16	12/13/16	12/13/16
005	12/09/16	Existing roof drain POC and routing	-	-	-	12/13/16
006	12/09/16	Existing to remain ceiling at B04	-	-	-	12/13/16
007	12/09/16	Existing ceiling type to be removed (provide info)	-	-	-	12/09/16
008R	12/21/16	Existing framing questions @ theatre low wall	RM Byrd	12/21/16	01/09/17	01/09/17
008R1	01/18/17	Existing framing questions @ theatre high wall	RM Byrd	01/18/17	01/19/17	01/23/17
009	12/20/16	Door and hardware questions (relates to submittals)	-	-	-	01/06/17
010	12/20/16	Storm drain question (no question)	-	-	-	12/23/16
011	02/01/17	Clarify availability floor return air grille beneath theater seating	CEDG	02/01/17	02/02/17	02/02/17
012	03/01/17	Wood door questions per submittal review	-	-	-	03/27/17
013	03/02/17	Theatre metal framing and bridging	RM Byrd	03/02/17	03/10/17	03/12/17
014	03/02/17	Theatre metal framing and existing wall track	RM Byrd	03/02/17	03/10/17	03/12/17

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
015	03/02/17	Metal framing at duct openings in theatre	Byrd/CEDG	3/3 & 3/14	03/15/17	03/15/17
015R1	03/17/17	Metal framing at duct openings in theatre	Byrd/CEDG	03/17/17	03/20/17	03/20/17
016	03/02/17	Existing plaster walls at both sides of stage	RM Byrd	03/03/17	03/17/17	03/17/17
017	03/02/17	Follow spot rooms framing and finish	-	-	-	03/08/17
018	03/02/17	Construction of the niches with existing work	RM Byrd	03/03/17	03/17/17	03/17/17
018R1	03/20/17	Construction of the niches with existing work	-	-	-	03/21/17
018R2	04/06/17	Construction of the niches with existing work	RM Byrd	04/06/17	04/11/17	04/11/17
018R3	05/22/17	Construction of the niches with existing work	RM Byrd	05/22/17	06/06/17	06/07/17
018R4	08/02/17	Construction of the niches with existing work	-	-	-	08/02/17
020	03/03/17	Ceiling heights at B13 & B114	-	-	-	03/03/17
021	03/03/17	Portland cement plaster per 09220	-	-	-	03/03/17
021R1	03/06/17	Portland cement plaster per 09220	-	-	-	03/08/17
022	03/07/17	Verify location of existing IDF (to remain?)	DCGA	03/07/17	03/09/17	03/12/17
023	03/10/17	Soils compaction at electrical trenches	RMA	03/10/17	03/14/17	03/14/17
024	03/13/17	Electrical and LV cabling/clocks/PA	DCGA	03/14/17	03/20/17	03/20/17
025	03/14/17	Hollow metal door and frame questions	-	-	-	03/17/17
025R1	03/27/17	Hollow metal door and frame questions	-	-	-	03/29/17
026	03/20/17	Existing ductwork demo at existing walls	-	-	-	03/23/17
026R1	03/28/17	Existing ductwork demo at existing walls	-	-	-	03/31/17
027	03/27/17	Existing damaged 4-inch fire water line	MSL	03/27/17	04/03/17	04/03/17
028	03/28/17	Existing grade beam at new sewer line	CEDG	03/28/17	03/30/17	03/30/17
029	03/28/17	New conduit entry elevation at ex. UG vault	DCGA	03/28/17	04/03/17	04/03/17
030	03/28/17	Locations for grilles at theatre side walls	-	-	-	03/30/17
031	03/28/17	New wood strips at acoustical wall panels	-	-	-	03/30/17
032	03/28/17	Trench detail for Kitchen underground	CEDG	03/28/17	04/03/17	04/03/17
033	03/28/17	Sand bedding in lieu of 3/8" pea gravel	MSL	03/29/17	03/29/17	03/29/17
034	03/29/17	Floor drain at kitchen	CEDG	03/29/17	04/03/17	04/03/17

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
035	04/06/17	Existing soil conditions	MSL	04/06/17	04/11/17	04/11/17
036	04/06/17	Grease trap permitting	CEDG	04/06/17	04/10/17	04/10/17
037	04/06/17	Suspected ACM at cafeteria	-	-	-	04/10/17
038	04/06/17	Duct liner R values	CEDG	04/06/17	04/10/17	04/10/17
039	04/07/17	Electrical conduit and feed to Bldg E	DCGA	04/07/17	04/11/17	04/11/17
040	04/11/17	Cafeteria fire sprinkler	JH	04/11/17	04/17/17	04/17/17
040R1	04/18/17	Cafeteria fire sprinkler	JH	04/18/17	04/24/17	04/25/17
040R2	05/08/17	Cafeteria fire sprinkler	IMEG			05/08/17
041	04/10/17	Site wall footings and rebar	RM Byrd	04/10/17	04/11/17	04/11/17
042	04/19/17	Supply registers at theatre walls	CEDG	04/19/17	04/28/17	05/01/17
043	04/19/17	Floor sink at walk-ins	L&S	04/19/17	05/01/17	05/01/17
044	04/19/17	Pipe wrap for UG piping	CEDG	04/19/17	04/19/17	04/19/17
045	04/19/17	Request for wall types	-	-	-	05/05/17
045R1	04/19/17	Request for wall types	-	-	-	05/08/17
046	04/19/17	Vent in wall location at kitchen	CEDG	04/19/17	04/21/17	04/24/17
046R1	05/02/17	Vent in wall location at kitchen	CEDG/L&S	05/02/17	05/04/17	05/04/17
047	04/19/17	Cafeteria volumn dampers	CEDG	04/19/17	04/24/17	04/24/17
048	04/19/17	Hangers at stage	CEDG	04/19/17	04/24/17	04/24/17
048R1	09/01/17	Hangers at stage	CEDG	09/11/17	09/18/17	09/18/17
048R2	09/28/17	Hangers at stage	RM Byrd	09-29-017	09/29/17	10/02/17
049	04/20/17	Riser hangers	CEDG	04/19/17	04/24/17	04/24/17
050	04/20/17	Riser length on MB3.1	CEDG	04/19/17	04/19/17	04/20/17
051	04/20/17	Existing finishes at new steel supports	-	-	-	05/05/17
052	04/20/17	Reinforcing bars at wall footings	RM Byrd	04/19/17	04/19/17	04/20/17
053	04/20/17	Existing wall condition at new door openings	RM Byrd	04/19/17	05/05/17	05/05/17
054	04/20/17	Obstructions at (n) steel columns and beams	-	-	-	05/08/17
055	04/24/17	Concrete anchor type	RM Byrd	04/24/17	04/25/17	04/25/17

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
056	04/26/17	Existing fire line condition	MSL	04/28/17	05/01/17	05/01/17
057	04/26/17	Ex. conditions effecting Str. Steel install (13)	DCGA	04/26/17	05/08/17	05/08/17
058	04/26/17	Ex. conditions effecting Str. Steel install (14)	-	-	-	05/06/17
059	04/26/17	Ex. conditions effecting Str. Steel install (12)	-	-	-	05/06/17
060	04/26/17	Ex. conditions effecting Str. Steel install (11&4)	-	-	-	05/06/17
061	04/26/17	Unknown ex. gas line questions	MSL/CEDG	04/28/17	05/01/17	05/05/17
062	04/27/17	Ex. conditions effecting Str. Steel install (10)	-	-	-	05/06/17
063	04/27/17	Ex. conditions effecting Str. Steel install (9)	DCGA	04/28/17	05/08/17	05/08/17
064	04/27/17	Ex. conditions effecting Str. Steel install (8)	DCGA	04/28/17	05/08/17	05/08/17
065	04/27/17	Ex. conditions effecting Str. Steel install (1)	-	-	-	05/06/17
066	04/27/17	Ex. conditions effecting Str. Steel install (2)	-	-	-	05/10/17
067	04/27/17	Ex. conditions effecting Str. Steel install (3&5)	-	-	-	05/06/17
068	04/28/17	Locations for step footings	RM Byrd	04/28/17	04/28/17	05/01/17
069	04/28/17	Ex. conditions effecting Str. Steel install (6)	-	-	-	05/10/17
070	04/28/17	Existing sewer line condition	MSL	04/28/17	05/01/17	05/01/17
071	05/03/17	New west wall at kitchen	-	-	-	05/08/17
072	05/02/17	Floor drain at room B-16	CEDG/L&S	05/03/17	05/04/17	05/04/17
073	05/15/17	Compression post stud in lieu of post	-	-	-	05/17/17
074	05/15/17	Cafeteria south wall window openings	-	-	-	05/19/17
075	05/22/17	Existing condition @ concrete column	RM Byrd	05/22/17	05/23/17	05/23/17
076	05/22/17	(N) double doors at existing openings, theatre	-	-	-	05/24/17
077	05/22/17	Ex. Pipes at cafeteria soffit above new door openings	-	-	-	05/24/17
077R1	06/02/17	Ex. Pipes at cafeteria soffit above new door openings	-	-	-	06/02/17
078	06/02/17	Radius origin point discrepancy (rev)	-	-	-	06/07/17
079	06/02/17	HVAC shaft encroachs on window Rm B109	CEDG	06/02/17	06/06/17	06/06/17

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
080	06/02/17	HVAC shaft encroachs on window Rm B113	CEDG	06/02/17	06/06/17	06/06/17
081	06/13/17	Piping note clarification	CEDG	06/13/17	06/13/17	06/13/17
082	06/15/17	Ex. Electrical conduit interference	DCGA	06/15/17	06/19/17	06/19/17
083	06/15/17	Ex. Utility lines interfere with SS installation	CEDG/IMEG	06/15/17	06/21/17	06/22/17
084	06/19/17	Depressed Kitchen concrete slab	RM Byrd	06/19/17	06/19/17	06/19/17
085	06/21/17	Ex Fire sprinkler lines interference with ceiling	IMEG	06/21/17	06/22/17	06/22/17
086	06/28/17	Column connection to ex pier	RM Byrd	06/28/17	06/28/17	06/28/17
087	06/29/17	Cafeteria ceiling finish at existing alcoves	-	-	-	07/06/17
088	06/29/17	Kitchen wall dimension between columns	-	-	-	07/03/17
089	06/29/17	Fire damper at rated wall in cafeteria	-	-	-	07/06/17
090	06/29/17	Ex. opening at new fire damper at cafeteria	-	-	-	07/03/17
091	06/29/17	Existing opening and new duct requirement	CEDG	06/29/17	07/05/17	07/05/17
092	06/29/17	Ex. floor opening and new duct requirement	CEDG	06/29/17	07/05/17	07/05/17
092R1	07/24/17	Ex. floor opening and new duct requirement	CEDG		07/24/17	07/24/17
093	06/30/17	Box boom mounting and clearance	Ruzika	06/30/17	07/10/17	07/10/17
094	07/05/17	Laminate color selection with kitchen equipmt	-	-	-	07/10/17
095	07/12/17	Kitchen hoods questions	L&S	07/13/17	07/18/17	07/18/17
096	07/12/17	HVAC branch line configuration	CEDG	07/13/17	07/18/17	07/18/17
097	07/17/17	Fire extinguisher type clarification	-	-	-	07/18/17
098	07/25/17	Heat detector in attic space of Bldg A	DCGA	07/25/17	07/25/17	07/26/17
098R1	07/27/17	Heat detector in attic space of Bldg A	DCGA	07/27/17	07/27/17	07/27/17
099	07/25/17	Existing window in new wall at Kitchen	-	-	-	07/31/17
099R1	08/01/17	Existing window in new wall at Kitchen	-	-	-	08/01/17
101	07/28/17	Fire damper access mech room	CEDG	07/28/17	08/01/17	08/02/17
102	07/28/17	Insulation in walls	-	-	-	08/02/17
103	08/02/17	Ceiling heights at foyers and dressing room	-	-	-	08/02/17
104	08/03/17	Conduit runs to TR-AV and ELI-1	DCGA/WLC	08/03/17	08/09/17	08/09/17
105	08/04/17	Substituted Speaker Assembly Supports	RM Byrd	08/10/17	08/30/17	08/30/17

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
106	08/07/17	Existing work conflict at structural steel install	IMEG/CEDG	08/07/17	08/10/17	08/10/17
107	08/10/17	Roof support framing anchorage	RM Byrd	08/10/17	08/28/17	08/28/17
108	08/14/17	Sheet vinyl patterns and logos	-	-	-	08/25/17
109	08/14/17	Steel beam to column connection	RM Byrd	08/14/17	08/21/17	08/21/17
110	08/15/17	Theatre equipment custom finishes	Ruzika	08/23/17	08/25/17	08/25/17
111	08/16/17	Kitchen roll-down door mounting	-	-	-	08/28/17
111R1	08/28/17	Kitchen roll-down door mounting	-	-	-	08/29/17
112	08/16/17	Wall at kitchen room B23A	-	-	-	08/28/17
113	08/16/17	Ex. wall condition at north mech. Room B04	-	-	-	08/28/17
113R1	09/11/17	Ex. wall condition at north mech. Room B04	RM Byrd	09/11/17	09/14/17	09/14/17
114	08/17/17	Existing pipes below new ceiling in B-24 Servery	-	-	-	08/28/17
115	08/28/17	Duct openings in balcony plenums	CEDG	08/28/17	08/29/17	08/29/17
116	08/28/17	Foyer ceiling heights at mechanical	CEDG	08/28/17	08/30/17	08/30/17
117	08/28/17	Relief vent at kitchen	CEDG	08/28/17	09/07/17	09/07/17
118	08/28/17	Property room wall layout	CEDG	08/30/17	09/11/17	09/11/17
119	08/28/17	Loading platform layout	Ruzika	09/01/17	09/07/17	09/08/17
120	08/29/17	Follow spot wall at projection room	-	-	-	09/01/17
121	08/29/17	Window head, sill, jamb at kitchen windows	-	-	-	09/01/17
122	08/29/17	Dimmer rack locations	DCGA/Ruzika	09/01/17	09/11/17	09/11/17
123	09/01/17	18x18" OSA louver in window at B21	CEDG	09/01/17	09/11/17	09/11/17
124	09/22/17	Existing fire cabinet line at Cafeteria	IMEG	09/22/17	09/25/17	09/25/17
125	09/01/17	Ceiling lay out at cafeteria	-	-	-	09/05/17
126	09/22/17	Fire sprinkler drain line at kitchen	CEDG	09/22/17	09/27/17	09/27/17
127	09/08/17	Relief air plenum at B02	CEDG	09/08/17	09/11/17	09/11/17
128	09/11/17	Exhaust fan in B08	CEDG	09/11/17	09/19/17	09/20/17
129	09/15/17	Fire Alarm field changes at building D	DCGA	09/18/17	09/20/17	09/21/17
130	09/21/17	Existing refriger line at existing window opening	-	-	-	09/25/17
131	09/21/17	Light source option	DCGA	09/21/17	09/25/17	*

REQUEST FOR INFORMATION LOG

John Muir High School Modernization

Pasadena Unified School District

Contractor: The Nazerian Group

Construction Manager: N/A

Project No.:

RFI NO.	DATE REC'D	DESCRIPTION	REFERRED TO CONSULTANT	DATE SENT	DATE RET'D	REPLY DATE
132	09/27/17	Rated lighting enclosures	DCGA		10/03/17	10/03/17
133	09/27/17	Building D F.A. flow switch	IMEG/DCGA	09/27/17	09/28/17	09/28/17
134	09/27/17	Building D F.A. at elevator	DCGA	09/28/17	10/03/17	10/03/17
134R1	10/05/17	Building D F.A. at elevator	DCGA	10/06/17		
135	09/28/17	New openings in existing concrete at B-1	CEDG	09/29/17		
136	09/28/17	Door opening at kitchen	-	-	-	10/02/17
137	09/28/17	Mechanical openings at projection room	CEDG	09/29/17		
138	09/28/17	Isolators for fan coil 8	CEDG	09/29/17		
139	10/06/17	Smoke dampers at stage attic				
140	10/06/17	Ceiling height at Fan Coil 5				
141	10/06/17	Retaining wall detail 20/SO.2 question				

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish
WOOD AND PLASTICS						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
06-01.311	Rough Carpentry(Pending RFI)	54	135	0	03APR17A	06OCT17
DOORS AND WINDOWS						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
08-06.300	DOOR FRAME INSTALLATION	5	5	0	31OCT17	06NOV17
08-08.300	DOORS & HARDWARE INST.	10	10	0	06DEC17	19DEC17
FINISHES						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
09-02.300	HANG DRYW. MUD & TAPE	66	75	0	22AUG17A	04DEC17
09-01.320	PAINTING	19	19	0	05DEC17	29DEC17
09-01.380	FIRE EXTINGUISHER CABINET	2	2	0	04JAN18	05JAN18
09-01.350	ACOUST. CIELING TILE INST.	10	10	0	22JAN18	02FEB18
09-01.340	CASEWORK INST.	10	10	0	02FEB18	15FEB18
09-01.360	INST.FLOOR.AUDIT. CAFETE.	21	21	0	19FEB18	19MAR18
09-01.390	STAGE FLOORING DEMO	3	3	0	28FEB18	02MAR18
09-01.400	STAGE FLOORING INST.	10	10	0	05MAR18	16MAR18
09-01.370	FINAL CLEAN UP	3	3	0	16APR18	18APR18
SPECIALTIES						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
10-04.300	FIRE SPRINKLER	10	43	0	01AUG17A	28SEP17
10-03.310	THEATRICAL RIGGING	21	21	0	01DEC17	29DEC17
10-03.300	CUSTOM GRAPHIC	9	9	0	04DEC17	14DEC17
10-03.320	AUDIT.ACOUST.TREATMENT	16	16	0	15DEC17	05JAN18
EQUIPMENT						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
11-01.300	AUDIO VISUAL EQUIP.INST.	10	10	0	19MAR18	30MAR18
CONST.ACTIVITIES @AUDIT.&KITCHEN						
11-01.310	BLEACHER REPLACEMENT	32	0	100	31OCT16A	28JUL17A
11-01.330	SHOPDRAWING AND SUBM.	20	0	100	31OCT16A	25NOV16A
11-01.340	DSA SUBMITALL	3	0	100	28NOV16A	30NOV16A
11-01.350	DSA REVIEW & APPROVAL	104	0	100	30NOV16A	18APR17A
11-01.360	BLEACHER FABRICATION	15	0	100	15JUN17A	27JUL17A
11-01.370	EXIST.BLEACHER DEMO	15	0	100	27JUL17A	28JUL17A
11-01.380	NEW BLEACHER INST.	41	0	100	09AUG17A	25AUG17A

Rough Carpentry(Pending RFI)

DOOR FRAME INSTALLATION
DOORS & HARDWARE INST.

HANG DRYW. MUD & TAPE
PAINTING
FIRE EXTINGUISHER CABINET
ACOUST. CIELING TILE INST.
CASEWORK INST.

INST.FLOOR.AUDIT. CAFETE.
STAGE FLOORING DEMO
STAGE FLOORING INST.
FINAL CLEAN UP

CEILING GRID INST.
KITCHEN FLOORING

FIRE SPRINKLER
THEATRICAL RIGGING
CUSTOM GRAPHIC
AUDIT.ACOUST.TREATMENT

AUDIO VISUAL EQUIP.INST.

BLEACHER REPLACEMENT

SHOPDRAWING AND SUBM.

DSA SUBMITALL

DSA REVIEW & APPROVAL

BLEACHER FABRICATION

EXIST.BLEACHER DEMO


NEW BLEACHER INST.

Sheet 2 of 3

M.H.S.MOD.
Updated
Schedule
Sept.10 ,2017

16SEP16
16SEP16
10SEP17 17:52

The Nazerian Group
Muir H.S.
Modernization

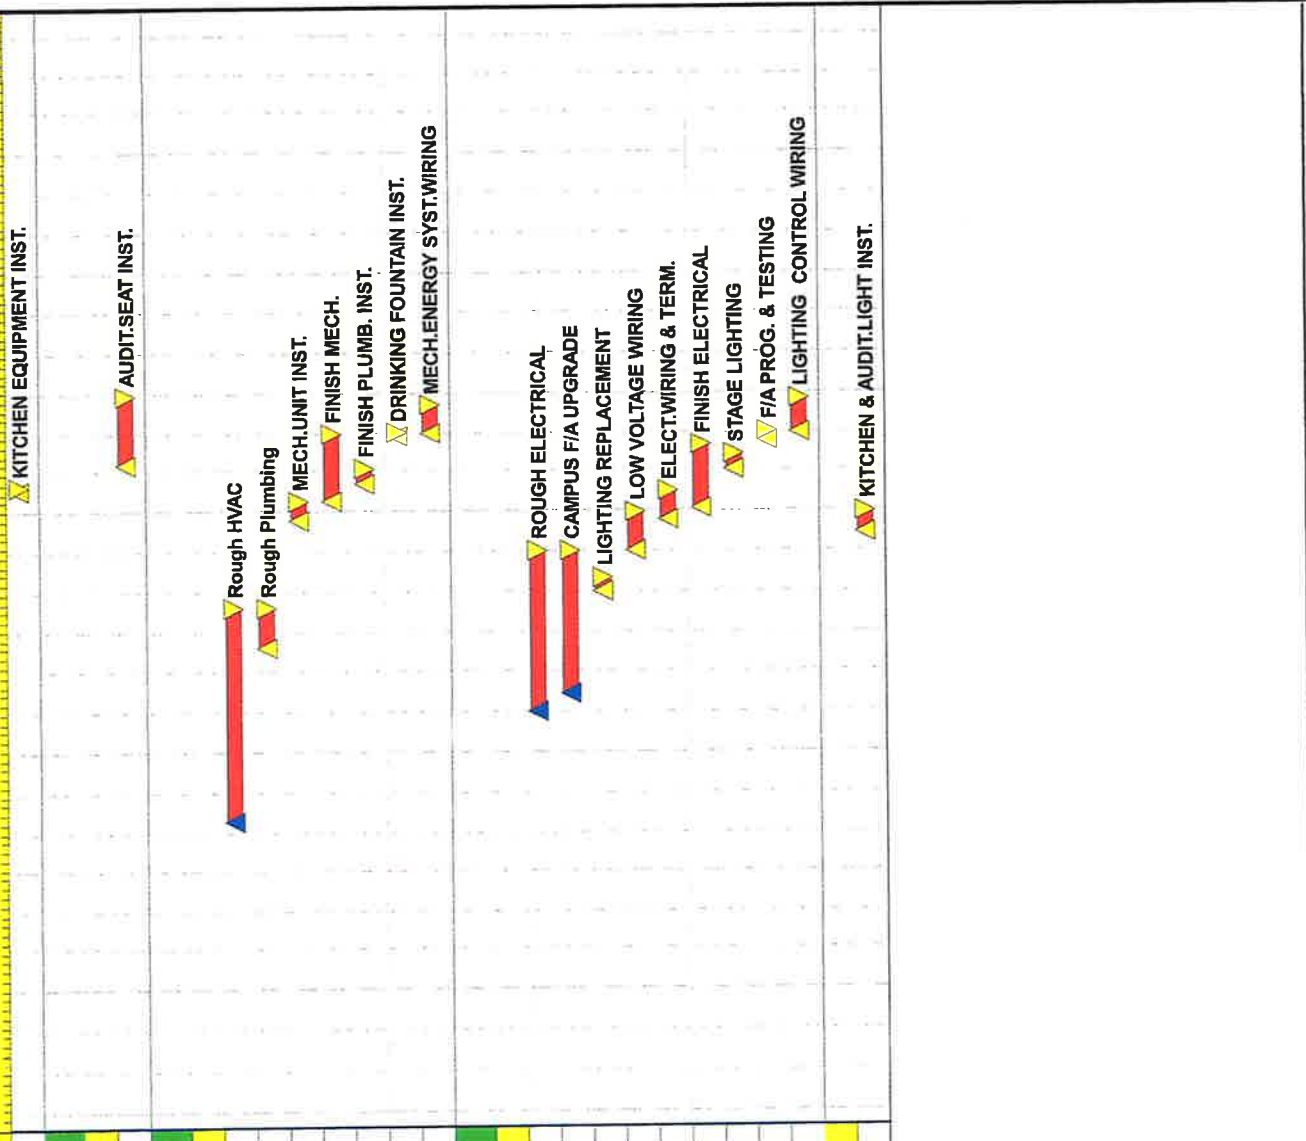

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish
11-01.320	KITCHEN EQUIPMENT INST.	2	2	0	18JAN18	19JAN18
FURNISHING AND SEATING						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
12-01.300	AUDIT.SEAT INST.	40	40	0	05FEB18	30MAR18
MECHANICAL & PLUMBING						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
15-02.300	Rough HVAC	17	119	0	10MAY17A	18OCT17
15-01.310	Rough Plumbing	23	23	0	18SEP17	18OCT17
15-02.350	MECH.UNIT INST.	11	11	0	25DEC17	08JAN18
15-02.390	FINISH MECH.	37	37	0	09JAN18	28FEB18
15-02.400	FINISH PLUMB. INST.	10	10	0	22JAN18	02FEB18
15-02.380	DRINKING FOUNTAIN INST.	3	3	0	28FEB18	02MAR18
15-02.340	MECH.ENERGY SYST.WIRING	16	16	0	01MAR18	22MAR18
ELECTRICAL						
CONST.ACTIVITIES @AUDIT.&KITCHEN						
16-02.380	ROUGH ELECTRICAL	45	88	0	01AUG17A	30NOV17
16-02.320	CAMPUS F/A UPGRADE	75	315	0	14AUG17A	30NOV17
16-01.310	LIGHTING REPLACEMENT	8	8	0	01NOV17	10NOV17
16-02.350	LOW VOLTAGE WIRING	21	21	0	01DEC17	29DEC17
16-02.360	ELECT.WIRING & TERM.	16	16	0	25DEC17	15JAN18
16-02.310	FINISH ELECTRICAL	35	35	0	02JAN18	19FEB18
16-01.330	STAGE LIGHTING	8	8	0	01FEB18	12FEB18
16-02.370	F/A PROG. & TESTING	5	5	0	23FEB18	01MAR18
16-02.300	LIGHTING CONTROL WIRING	18	18	0	01MAR18	26MAR18
16-01.380	KITCHEN & AUDIT.LIGHT INST.	11	11	0	15DEC17	29DEC17

Start Date: 16SEP16
 Data Date: 16SEP16
 Run Date: 10SEP17 17:52

M.H.S.MOD.
 Updated Schedule
 Sept. 10, 2017

The Nazerian Group
 Muir H.S.
 Modernization

Sheet 3 of 3

Date	Revision	Checked	Approved

© Primavera Systems, Inc.
